


Eighth Edition

PMBOK[®]

Guide

A Guide to the
Project Management
Body of Knowledge

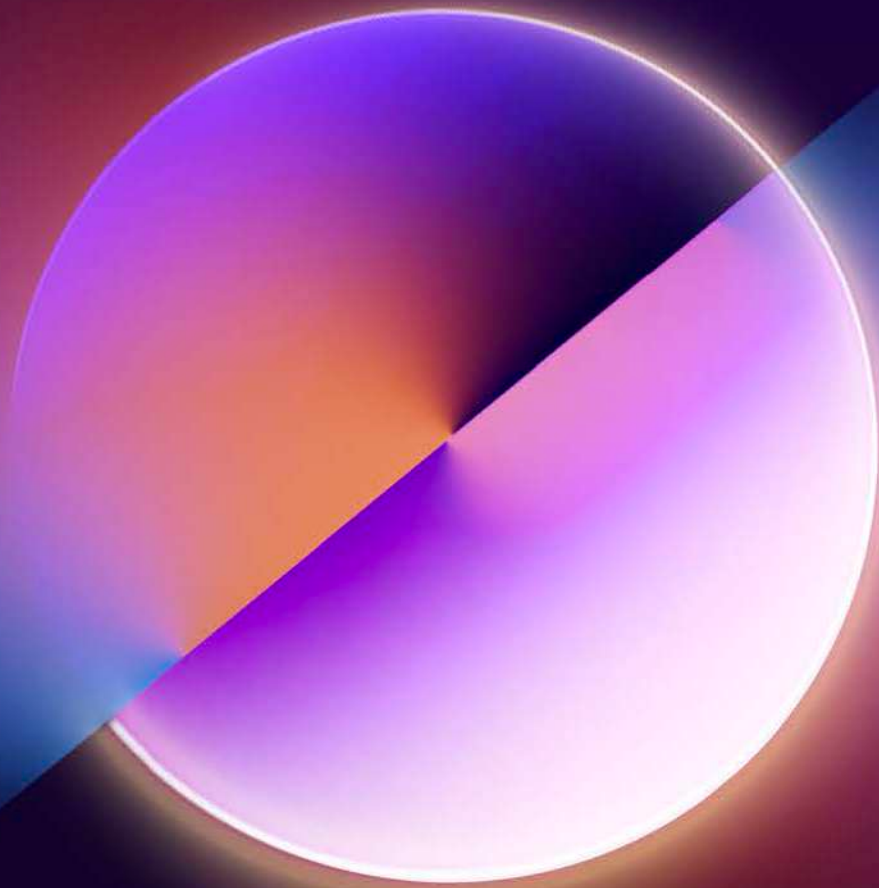

Includes **The Standard for Project Management**

The Standard for Project Management

and

A Guide to the Project Management Body of Knowledge

PMBOK® Guide
Eighth Edition



Notice

The Project Management Institute, Inc. (PMI) standards and guideline publications, of which the document contained herein is one, are developed through a voluntary consensus standards development process. This process brings together volunteers and/or seeks out the views of persons who have an interest in the topic covered by this publication. While PMI administers the process and establishes rules to promote fairness in the development of consensus, it does not write the document and it does not independently test, evaluate, or verify the accuracy or completeness of any information or the soundness of any judgments contained in its standards and guideline publications.

PMI disclaims liability for any personal injury, property or other damages of any nature whatsoever, whether special, indirect, consequential or compensatory, directly or indirectly resulting from the publication, use of application, or reliance on this document. PMI disclaims and makes no guaranty or warranty, expressed or implied, as to the accuracy or completeness of any information published herein, and disclaims and makes no warranty that the information in this document will fulfill any of your particular purposes or needs. PMI does not undertake to guarantee the performance of any individual manufacturer or seller's products or services by virtue of this standard or guide.

In publishing and making this document available, PMI is not undertaking to render professional or other services for or on behalf of any person or entity, nor is PMI undertaking to perform any duty owed by any person or entity to someone else. Anyone using this document should rely on his or her own independent judgment or, as appropriate, seek the advice of a competent professional in determining the exercise of reasonable care in any given circumstances. Information and other standards on the topic covered by this publication may be available from other sources, which the user may wish to consult for additional views or information not covered by this publication.

PMI has no power, nor does it undertake to police or enforce compliance with the contents of this document. PMI does not certify, test, or inspect products, designs, or installations for safety or health purposes. Any certification or other statement of compliance with any health or safety-related information in this document shall not be attributable to PMI and is solely the responsibility of the certifier or maker of the statement.

Table of Contents

The Standard for Project Management

Preface	vii
Evidence-Based and Globally Represented.	vii
Summary of Changes.	vii
Update of Key Terms and Concepts	viii
Refined Principles.	viii
Reintroducing Process Groups as Focus Areas.	viii
Updated Performance Domains	ix
1 Introduction	3
1.1 Purpose of <i>The Standard for Project Management</i>	3
1.2 Key Terms and Concepts.	4
1.3 Foundational Elements of Project Management	6
1.3.1 Characteristics of a Project	6
1.3.2 Connecting Organizational Governance and Project Governance	7
1.3.3 Operations and Project Management.	9
1.3.4 Relationship of Portfolio, Program, Project, and Operations Management	10
2 A System for Value Delivery	13
2.1 Creating Value.	13
2.1.1 Value Delivery Components	15
2.1.2 Assessing Project Success	16
2.2 Project Environment	17
2.2.1 Enterprise Environmental Factors	18
2.2.2 Organizational Process Assets	19
2.2.3 Policies, Processes, and Procedures	20
2.2.4 Organizational Knowledge Repositories.	21
2.2.5 Organizational Structures	21

2.3 Product Management Considerations	21
2.4 Functions Associated With Projects	24
2.4.1 Provide Oversight and Coordination	25
2.4.2 Solicit and Manage Feedback	25
2.4.3 Facilitate and Support	26
2.4.4 Perform Work	26
2.4.5 Apply Expertise	26
2.4.6 Provide Organizational Direction and Insight	26
2.4.7 Provide Resources	27
2.5 Project Management Roles	27
2.5.1 Project Management Team	27
2.5.2 Sponsor, Customer, or Product Owner	32
2.5.3 Project Team	33
2.5.4 End Users and Other Key Stakeholders	33
3 Project Management Principles	35
3.1 The Project Management Mindset	36
3.2 Principles and Performance Domains	37
3.3 Adopt a Holistic View.	38
3.3.1 Project Impact	38
3.3.2 Principle in Action.	39
3.3.3 Connected Performance Domains	39
3.4 Focus on Value	40
3.4.1 Project Impact	41
3.4.2 Principle in Action.	42
3.4.3 Connected Performance Domains	42
3.5 Embed Quality Into Processes and Deliverables	43
3.5.1 Project Impact	44
3.5.2 Principle in Action.	45
3.5.3 Connected Performance Domains	45
3.6 Be an Accountable Leader	46
3.6.1 Project Impact	47
3.6.2 Principle in Action.	48
3.6.3 Connected Performance Domains	48

3.7 Integrate Sustainability Within All Project Areas	48
3.7.1 Project Impact	50
3.7.2 Principle in Action	52
3.7.3 Connected Performance Domains.....	52
3.8 Build an Empowered Culture.....	53
3.8.1 Project Impact	54
3.8.2 Principle in Action.....	54
3.8.3 Connected Performance Domains	55
4 Project Life Cycles	57
4.1 Project Phases	57
4.2 Project Development Approaches	59
4.2.1 Predictive Approaches	61
4.2.2 Adaptive Approaches.....	63
4.2.3 Hybrid Approaches.....	65
4.3 Considerations for a Development Approach Selection	67
4.3.1 Deliverables	67
4.3.2 Project.....	68
4.3.3 Organization	68
4.4 Delivery Cadence.....	69
4.5 Project Management Focus Areas	69
4.5.1 Initiating Focus Area.....	70
4.5.2 Planning Focus Area.....	70
4.5.3 Executing Focus Area.....	72
4.5.4 Monitoring and Controlling Focus Area	72
4.5.5 Closing Focus Area	72
4.5.6 Focus Areas as a Whole	73
References.....	75
Index.....	77

A Guide to the Project Management Body of Knowledge (PMBOK® Guide)

1 Introduction	3
1.1 Structure of the <i>PMBOK® Guide</i>	3
1.2 Relationship of the <i>PMBOK® Guide</i> and <i>The Standard for Project Management</i>	4
1.3 Changes to the <i>PMBOK® Guide</i>	5
1.4 Relationship to PMStandards+®	5
2 Project Management Performance Domains	7
2.1 Governance Performance Domain	10
2.1.1 Project Value Creation	10
2.1.2 Project Governance Models	11
2.1.3 Metrics and Mechanisms for Effective Project Governance	13
2.1.4 Additional Considerations for Predictive Environments	13
2.1.5 Key Concepts	14
2.1.6 Processes	15
2.1.7 Tailoring Considerations	33
2.1.8 Interactions With Other Domains	35
2.1.9 Check Results	35
2.2 Scope Performance Domain	35
2.2.1 Key Concepts	35
2.2.2 Processes	39
2.2.3 Tailoring Considerations	44
2.2.4 Interactions With Other Domains	45
2.2.5 Check Results	46
2.3 Schedule Performance Domain	47
2.3.1 Key Concepts	47
2.3.2 Processes	48
2.3.3 Tailoring Considerations	55
2.3.4 Interactions With Other Domains	57
2.3.5 Check Results	57
2.4 Finance Performance Domain	58
2.4.1 Key Concepts	59
2.4.2 Processes	61
2.4.3 Tailoring Considerations	65
2.4.4 Interactions With Other Domains	66
2.4.5 Check Results	66

2.5 Stakeholders Performance Domain	67
2.5.1 Key Concepts	68
2.5.2 Processes	70
2.5.3 Tailoring Considerations	74
2.5.4 Interactions With Other Domains	77
2.5.5 Check Results.	78
2.6 Resources Performance Domain	79
2.6.1 Key Concepts	79
2.6.2 Processes	80
2.6.3 Tailoring Considerations	88
2.6.4 Interactions With Other Domains	91
2.6.5 Check Results.	92
2.7 Risk Performance Domain	92
2.7.1 Key Concepts	92
2.7.2 Processes	94
2.7.3 Tailoring Considerations	98
2.7.4 Interactions With Other Domains	101
2.7.5 Check Results.	102
3 Tailoring	103
3.1 Overview	103
3.2 Why Tailor?	104
3.3 What to Tailor	104
3.3.1 Life Cycle and Development Approach Selection	104
3.3.2 Processes	105
3.3.3 Engagement.	105
3.4 The Tailoring Process	105
3.4.1 Select Initial Development Approach	105
3.4.2 Tailor for the Organization	106
3.4.3 Tailor for the Project.	108
3.4.4 Implement Ongoing Improvement	109
3.5 Tailoring the Performance Domains.	110
3.6 Diagnostics	110
3.7 Summary	112
4 Inputs and Outputs	113
5 Tools and Techniques.	145

Appendix X1: Contributors and Reviewers.....	217
X1.1 Contributors and Reviewers.....	217
X1.2 PMI Team Members.....	231
Appendix X2: Project Management Offices.....	233
X2.1 Introduction.....	233
X2.2 The PMO Value Proposition.....	233
X2.3 Importance of Customer Centricity for a PMO.....	234
X2.4 PMO Type, Model, and Structure.....	234
X2.5 PMO Maturity Models.....	235
X2.6 Learn More About PMOs.....	236
Appendix X3: Artificial Intelligence.....	237
X3.1 Artificial Intelligence in the Project Context.....	237
X3.1.1 Strategies for AI Adoption.....	238
X3.1.2 State of the Market.....	239
X3.2 Common Use Cases.....	239
X3.3 Responsible Use and Ethical Concerns.....	239
X3.4 Suggested Resources.....	244
Appendix X4: Procurement.....	245
X4.1 Procurement Introduction.....	245
X4.2 Procurement Overview.....	246
X4.3 Make-or-Buy Analysis.....	246
X4.4 Procurement Strategy.....	247
X4.5 Bid Process and Documents.....	248
X4.6 Source Selection Analysis.....	249
X4.7 Source Selection Criteria.....	249
X4.8 Contract Type.....	250
X4.8.1 Fundamental Contract Models.....	251
X4.8.2 Emerging Trends in Contract Management.....	252
X4.9 Claims Administration.....	252
X4.9.1 Relevance to Project Managers.....	253
X4.9.2 Sensitivity of Legal Actions and Upholding Ethics Codes.....	254
Appendix X5: Evolution of the <i>PMBOK® Guide</i>.....	255
X5.1 Evidence-Based.....	255
X5.2 Changes in the Eighth Edition.....	257
X5.3 Sources for the Eighth Edition.....	257
X5.4 Refinement of Project Management Principles.....	257
References.....	261
Bibliography.....	263
Glossary.....	265
Index.....	277
